University of Exeter

COM2020 – Project Management and Planning

Week 2 Workshop

Facilitated by TA: Ridi, Namia, Oscar and Assylay

Today you will

University of Exeter

- Assign Scrum roles in your team
- Create a Product Backlog using user stories
- Estimate work using Planning Poker
- Plan Sprint 1
- Build a Scrum board to track development

Scrum Roles & Team Structure – 10mins

In Scrum, each role has a clear responsibility

Product Owner	• Decides what is built • Owns and prioritizes backlogs
Scrum Master	• Decides how the team works • Facilitates planning and removes blockers
Development team	• Builds and delivers the software • Makes technical decisions

Task 1

As a team:

- Assign one Product Owner
- Assign one Scrum Master
- Everyone else is Development Team
- Discuss the roles

Product Backlog & User Stories

Your MoSCoW features from Week 1, or selected project will now be rewritten as user stories.

User Story:- A short description of functionality from the user's perspective.

User Story Format:- *As a **[user]**, I want **[functionality]**, so that **[benefit]***

Example

✅ Good:- *As a **first-year student**, I want **to filter events by date**, so that **I can plan my week easily***

❌ Poor:- *Event filtering feature*

Product Backlog & User Stories – 20mins

University of Exeter

Task 2 : Create a table as shown below

Priority	User Story	MoSCoW
1	As a ___, I want ___ so that ___	Must
2		Must
3		Should
4		Should

Planning Poker – Estimating Work

University of Exeter

What is Planning Poker?

- A team activity to **estimate how big or difficult a user story is.**

How Planning Poker Works

1. Product Owner reads **one user story**
2. Team briefly discusses it
3. Everyone chooses a number **at the same time**
4. If numbers differ ⊠ discuss ⊠ vote again
5. Agree on **one final value**

Use these numbers only:

Value	What it means
1	Very small, very clear
2–3	Small, low difficulty
5	Medium effort or complexity
8	Hard or uncertain
13	Very hard, high risk

⊠ Bigger number = **more effort, more risk, or more uncertainty**

Planning Poker – Estimating Work – 20mins

University of Exeter

Task 3 : Create a table as shown below

Priority	User Story	Story Points
1	As a ___, I want ___ so that ___	5
2		8
3		3
4		13

Sprint Planning – 30mins

University of Exeter

Task 4: Sprint planning decides what your team commits to in Sprint 1 (coursework 1).

Task 1: Select Stories

From your estimated user stories:

- Choose 3–5 stories for Sprint 1
- Prioritise Must-have features
- Keep the scope realistic (do not overcommit)

Task 2: Define the Sprint Goal

Write one clear sentence:

By the end of Sprint 1, we will have…

Example:
A working login system with basic user profiles

Task 3: Break Stories into Tasks

For each selected story, list the technical tasks required.

Example

Story: User login

- Design login UI
- Create database table
- Implement authentication
- Write basic tests

Output:
A clear Sprint 1 commitment with defined tasks, ready for execution.

Scrum Board – 25mins

Task 5: A Scrum board shows how work moves during development.

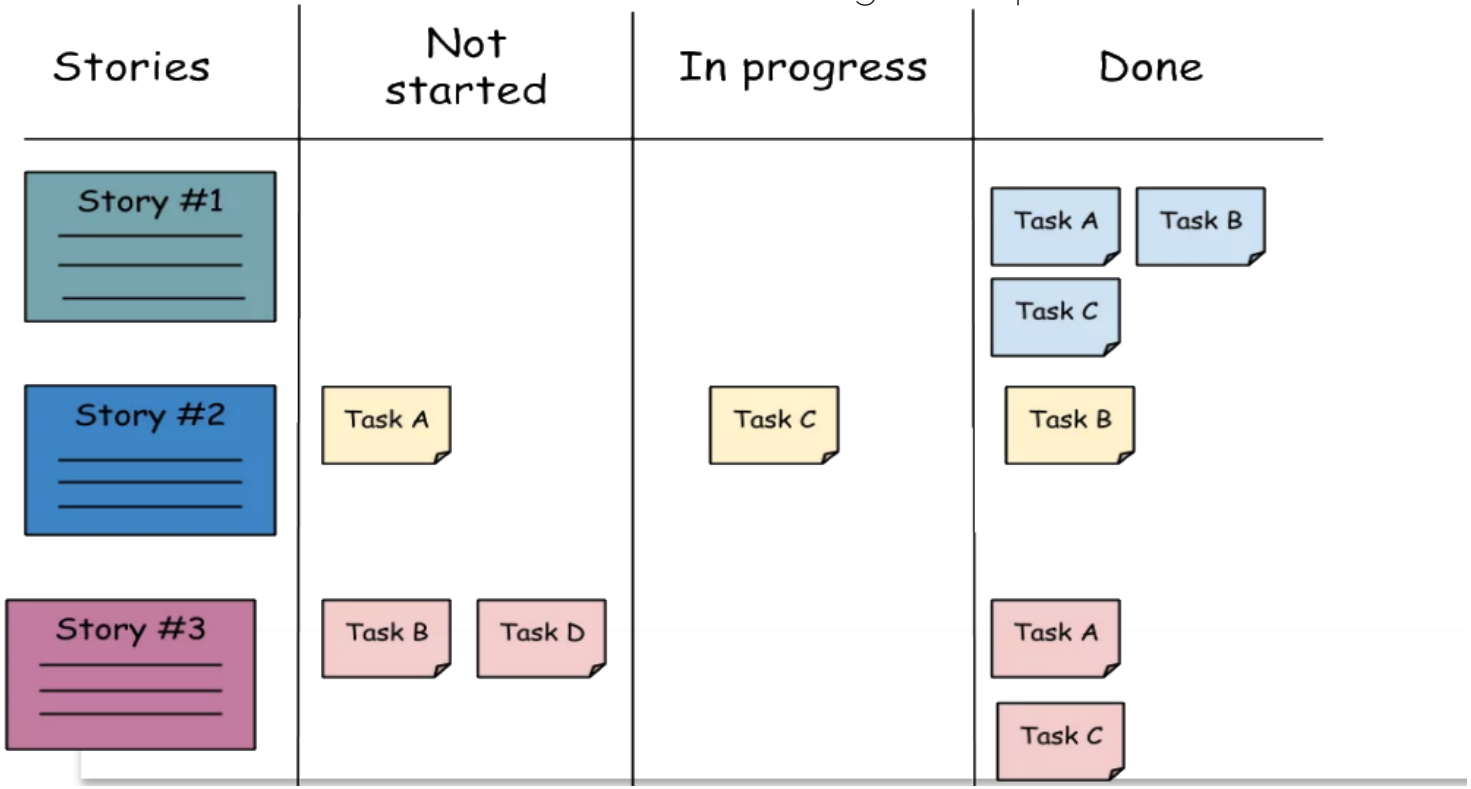

GitHub Repository Setup – 10mins

Task 6: Create your team's GitHub repository.

As a team:

- Create one shared GitHub repo
- Name it clearly ***(e.g. com2020-event-planner)***
- Add all team members as collaborators
- Create a README.md

README must include:

- Project title & short description
- Team members + roles
- Link to Scrum board (if digital)

Team Communication – 5mins

Task 7: Agree how your team will communicate

A clear communication and meeting plan

Decide and write down:

- Communication channel
- Weekly meeting time
- Responsible person (usually the Scrum Master)
